



SCV
WATER

September 19, 2023

ITEM NO.
6

General Operations Presentation



Board Meeting

Facility Upgrades


- CDF Conversion from Aqueous Ammonia to Liquid Ammonium Sulfate
- Galbreath Pressure Regulating Station Upgrades
- Well U6 Pump Removal




Castaic Disinfection Facility

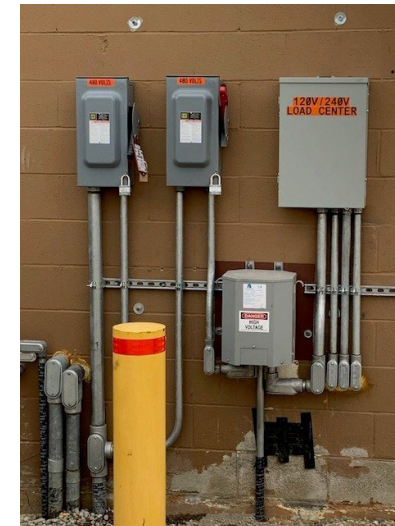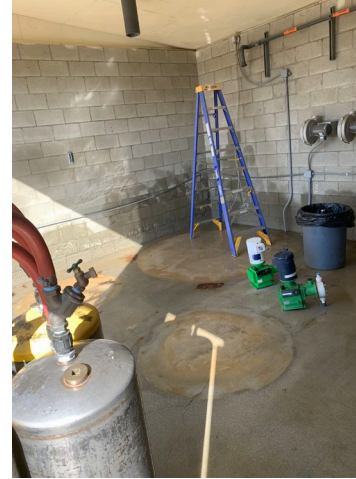


Castaic Disinfection Facility

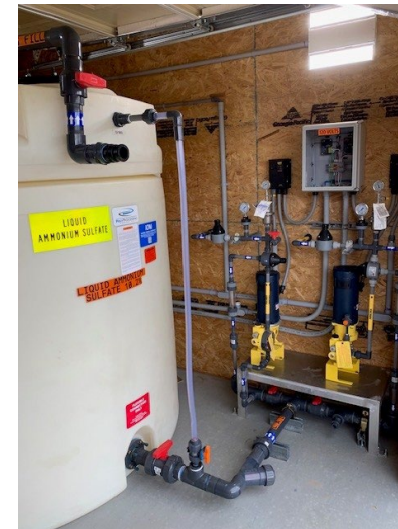


Galbreath Pressure Regulating Station

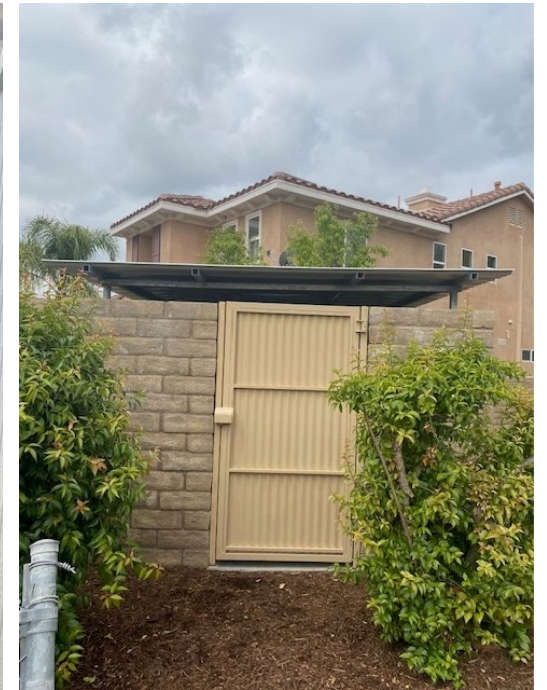

Facility Upgrades



Well 201 VOC Treatment Improvements Project Location Map

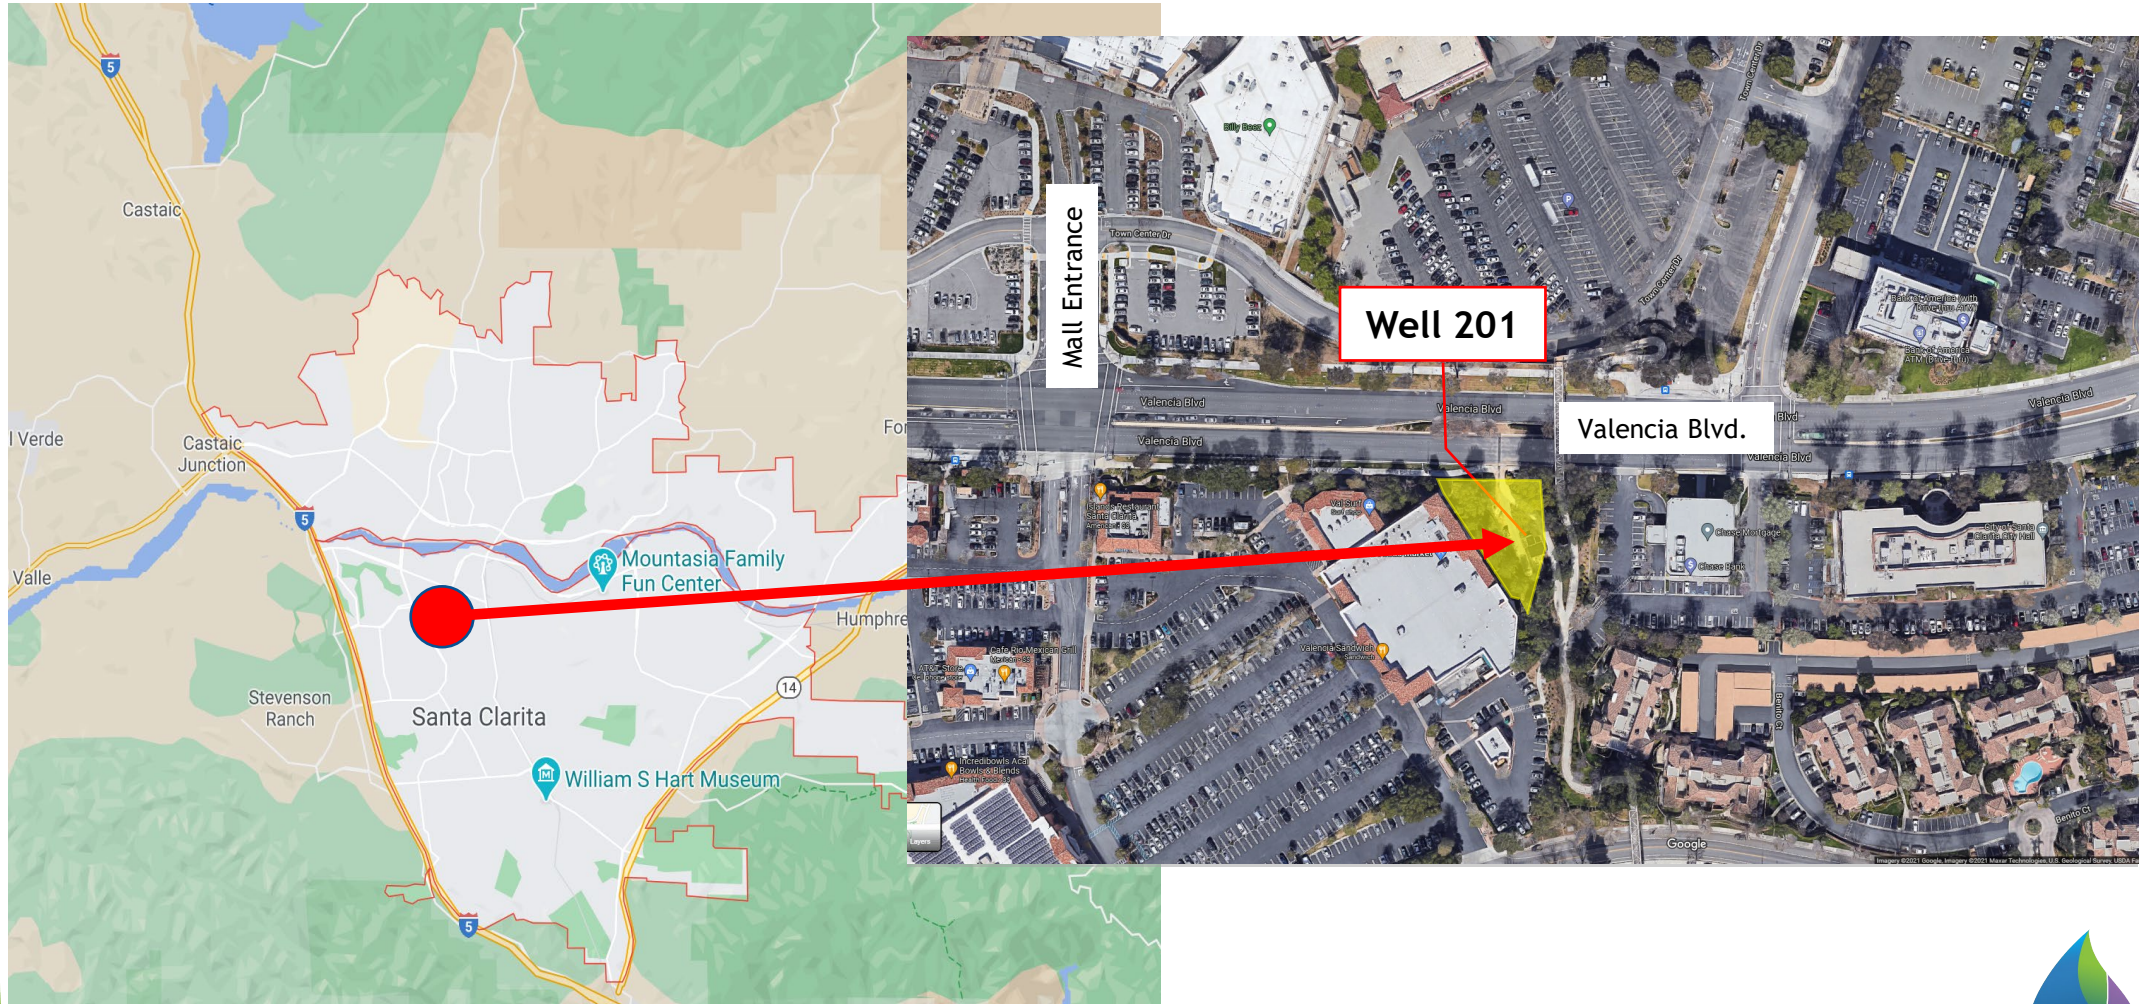

Well 201 Groundwater Treatment Project Status Update

Well 201 prior to construction:



Street View



Bird's Eye View



Well 201 Groundwater Treatment Project Status Update

- January 17, 2023: Board of Directors awarded Pacific Hydrotech Corporation the construction contract amount of \$7,726,700.
- February to June 2023: processing material submittals and ordering some of the materials.
- July 2023: Contractor mobilized onsite.
- September 2023: Construction is approximately 18% complete.
- February 2025: Anticipated construction completion.



Well 201 Groundwater Treatment Project Status Update



Installing formwork for Chemical Building Foundation



Well 201 Groundwater Treatment Project Status Update



24" drain line



Sodium Hypochlorite Tank Pad



Well 201 Groundwater Treatment Project Status Update



Installing formwork for underground
backwash tank



Valencia Boulevard view

Well 201 Groundwater Treatment Project Status Update



Overall site (September 18, 2023)



Well 201 Groundwater Treatment Project Status Update

Project 3-D Rendering:



Questions?

